Issue: 39/201224

Infrastructure Newsletter

Update



Cladding works

Below is a rough reschedule of the drilling for the first two weeks in January. Further details will be circulated as soon as we receive them.

W/C 06/01/25


- Monday
 - o Erection of Masts Elevation 2 level 6-8
 - o Install of Brackets and Rails Elevation 1
- Tuesday
 - o Erection of Masts Elevation 5 Level 4-Roof
 - o Install of Brackets and Rails Elevation 1
 - Anchor Drilling Elevation 2 all levels
- Wednesday
 - o Anchor Drilling Elevation 2 all levels and window protection
 - Erection of Masts Elevation 5 Level 4-Roof
- Thursday
 - o Anchor Drilling Elevation 2 all levels and window protection
 - o Erection of Masts Elevation 6 all floors
- Friday
 - o Anchor Drilling Elevation 2 all levels and window protection
 - o Erection of Masts Elevation 6 all floors

W/C 13/01/25

- Monday
 - Elevation 2, Bracket and Rail install
- Tuesday
 - o Elevation 2, Bracket and Rail install
- Wednesday
 - Elevation 2, Bracket and Rail install
- Thursday
 - Elevation 2, Bracket and rail install
- Friday
 - o Elevation 2, Bracket and Rail install

Issue: 39/201224



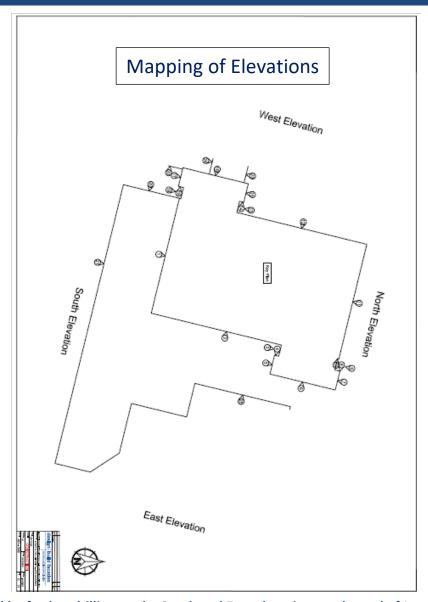

There will be further drilling on the South and East elevations at the end of January.

South Lift

We hope to have the south lift replaced by July 25. Until then, if you need anything moved please contact John Gillan on 07816609171.
